



ID	Task Name	Duration	Start	Finish	
1	FAA Project Coordination Meeting	1 day?	Mon 8/1/16	Mon 8/1/16	3%
2	<b>Project</b>	<b>446 days</b>	<b>Mon 9/12/16</b>	<b>Tue 6/12/18</b>	100%
3	Notice to Proceed	1 day	Mon 9/12/16	Mon 9/12/16	100%
4	<b>PART A - AIRPORT MASTER PLAN</b>	<b>308 days</b>	<b>Tue 9/13/16</b>	<b>Thu 11/30/17</b>	10%
5	<b>Task 1.0 - Prepare Study Design</b>	<b>5 days</b>	<b>Tue 9/13/16</b>	<b>Mon 9/19/16</b>	100%
6	<b>Task 2.0 - Mobilization</b>	<b>2 days</b>	<b>Tue 9/20/16</b>	<b>Wed 9/21/16</b>	90%
7	Task 2.1 - Conduct Kick-off Meeting and Presentation to Airport Authority	2 days	Tue 9/20/16	Wed 9/21/16	90%
8	<b>Task 3.0 - Stakeholder Involvement Program</b>	<b>285 days</b>	<b>Thu 9/22/16</b>	<b>Tue 11/7/17</b>	5%
9	<b>Task 4.0 - Environmental Considerations</b>	<b>10 days</b>	<b>Mon 1/9/17</b>	<b>Mon 1/23/17</b>	0%
10	<b>Task 5.0 - Inventory of Existing Conditions</b>	<b>15 days</b>	<b>Thu 9/29/16</b>	<b>Mon 10/20/16</b>	86%
11	Task 5.1 - Airport Background/History	5 days	Thu 9/29/16	Wed 10/5/16	100%
12	Task 5.2 - Review of Existing Aviation Plans and Studies	5 days	Thu 9/29/16	Wed 10/5/16	100%
13	Task 5.3 - Inventory and Description of Existing Facilities	5 days	Thu 10/6/16	Thu 10/13/16	100%
14	Task 5.4 - Tenant Interviews	3 days	Fri 10/14/16	Tue 10/18/16	100%
15	Task 5.5 - Collection of Historical Aviation Activity	5 days	Fri 10/14/16	Thu 10/20/16	100%
16	Task 5.6 - Collection of Socioeconomic Data	5 days	Fri 10/14/16	Thu 10/20/16	100%
17	Task 5.7 - Collection of Regional Setting and Land Use Data	3 days	Fri 10/14/16	Tue 10/18/16	100%
18	Task 5.8 - Inventory of Financial Information	5 days	Fri 10/14/16	Thu 10/20/16	0%
19	<b>Task 6.0 - Aviation Forecasts</b>	<b>35 days</b>	<b>Fri 10/21/16</b>	<b>Mon 12/12/16</b>	66%
20	Task 6.1 - Passenger Enplanements	2 days	Fri 10/21/16	Mon 10/24/16	100%
21	Task 6.2 - Air Cargo	3 days	Tue 10/25/16	Thu 10/27/16	100%
22	Task 6.3 - Aircraft Operations Forecast	<b>4 days</b>	<b>Tue 10/25/16</b>	<b>Fri 10/28/16</b>	100%
23	Task 6.3.1 - Fleet Mix Forecast	1 day	Fri 10/28/16	Fri 10/28/16	100%
24	Task 6.3.2 - Air Carrier and Commuter Operations	1 day	Tue 10/25/16	Tue 10/25/16	100%
25	Task 6.3.3 - General Aviation Aircraft Demand	1 day	Wed 10/26/16	Wed 10/26/16	100%
26	Task 6.4 - Peak (Design) Hour Forecasts	1 day	Mon 10/31/16	Mon 10/31/16	100%
27	Task 6.5 - Prepare Working Paper and Conduct Meetings	<b>28 days</b>	<b>Tue 11/1/16</b>	<b>Mon 12/12/16</b>	50%
28	Task 6.5.1 - Prepare Draft Working Paper #1	10 days	Tue 11/1/16	Tue 11/15/16	100%
29	Task 6.5.2 - Attend Coordination/Stakeholders Meeting	1 day	Wed 11/30/16	Wed 11/30/16	0%
30	Task 6.5.3 - Conduct Public Information Meeting	2 days	Wed 11/30/16	Thu 12/1/16	0%
31	Task 6.5.4 - Prepare Final Working Paper #1	7 days	Fri 12/2/16	Mon 12/12/16	0%
32	<b>Task 7.0 - Facility Requirements</b>	<b>49 days</b>	<b>Wed 11/16/16</b>	<b>Wed 1/25/17</b>	0%
33	Task 7.1 - Airfield Capacity Analysis	2 days	Wed 11/16/16	Thu 11/17/16	0%
34	Task 7.2 - Airfield and Airspace Requirements	<b>7 days</b>	<b>Fri 11/18/16</b>	<b>Tue 11/29/16</b>	0%
35	Task 7.2.1 - Runway Requirements	2 days	Fri 11/18/16	Mon 11/21/16	0%
36	Task 7.2.2 - Taxiways and Apron Requirements	3 days	Tue 11/22/16	Fri 11/25/16	0%
37	Task 7.2.3 - Visual and Electronic Navigational Aids	1 day	Mon 11/28/16	Mon 11/28/16	0%
38	Task 7.2.4 - Airspace Requirements	1 day	Tue 11/29/16	Tue 11/29/16	0%
39	Task 7.3 - Commercial Service Passenger Terminal Complex	10 days	Wed 11/30/16	Tue 12/13/16	0%
40	Task 7.4 - General Aviation Requirements	3 days	Tue 12/13/16	Thu 12/15/16	0%
41	Task 7.5 - Air Cargo Requirements	3 days	Tue 12/13/16	Thu 12/15/16	0%
42	Task 7.6 - Support Facilities	3 days	Tue 12/13/16	Thu 12/15/16	0%
43	Task 7.7 - Ground Access, Circulation, and Parking Requirements	10 days	Wed 11/30/16	Tue 12/13/16	0%
44	Task 7.8 - Workshop with Authority Staff	2 days	Wed 12/14/16	Thu 12/15/16	0%
45	Task 7.9 - Prepare Working Paper and Conduct Stakeholder Meeting	<b>28 days</b>	<b>Fri 12/16/16</b>	<b>Wed 1/25/17</b>	0%
46	Task 7.9.1 - Prepare Draft Working Paper #2	19 days	Fri 12/16/16	Wed 1/11/17	0%
47	Task 7.9.2 - Attend Coordination/Stakeholders Meeting	1 day	Wed 1/18/17	Wed 1/18/17	0%
48	Task 7.9.3 - Prepare Final Working Paper #2	5 days	Thu 1/19/17	Wed 1/25/17	0%
49	<b>Task 8.0 - Alternatives Development and Evaluation</b>	<b>83 days</b>	<b>Thu 1/19/17</b>	<b>Tue 5/16/17</b>	0%
50	Task 8.1 - Identification of Preliminary Alternatives	15 days	Thu 1/19/17	Wed 2/8/17	0%
51	Task 8.2 - Evaluation of Shortlist Alternatives	<b>40 days</b>	<b>Thu 2/9/17</b>	<b>Thu 4/6/17</b>	0%
52	Task 8.2.1 - Preliminary Cost Estimates	10 days	Thu 2/9/17	Thu 2/23/17	0%
53	Task 8.2.2 - Preliminary Financial Analysis	20 days	Fri 2/24/17	Thu 3/23/17	0%
54	Task 8.2.3 - Environmental Screening of Shortlisted Alternatives	10 days	Fri 3/24/17	Thu 4/6/17	0%
55	Task 8.3 - Selection of a Preferred Alternative	5 days	Fri 4/7/17	Thu 4/13/17	0%
56	Task 8.4 - Prepare Working Paper and Conduct Meetings	<b>17 days</b>	<b>Fri 4/14/17</b>	<b>Mon 5/8/17</b>	0%
57	Task 8.4.1 - Prepare Draft Working Paper #3	10 days	Fri 4/14/17	Thu 4/27/17	0%
58	Task 8.4.2 - Attend Coordination/Stakeholders Meeting	1 day	Fri 4/28/17	Fri 4/28/17	0%
59	Task 8.4.3 - Conduct Public Information Meeting	1 day	Mon 5/1/17	Mon 5/1/17	0%
60	Task 8.4.4 - Prepare Final Working Paper #3	5 days	Tue 5/2/17	Mon 5/8/17	0%
61	Task 8.5 - Authority Presentation #1	1 day	Tue 5/16/17	Tue 5/16/17	0%


Task		Summary		External Milestone		Inactive Summary		Manual Summary Rollup		Finish-only		Manual Progress	
Split		Project Summary		Inactive Task		Manual Task		Manual Summary		Deadline			
Milestone		External Tasks		Inactive Milestone		Duration-only		Start-only		Progress			

ID	Task Name	Duration	Start	Finish
62	<b>Task 9.0 - Airport Layout Plans</b>	<b>55 days</b>	<b>Wed 5/17/17</b>	<b>Thu 8/3/17</b>
63	Task 9.1 - Airport Layout Plan Drawing Set	40 days	Wed 5/17/17	Thu 7/13/17
64	Task 9.2 - Coordination and Submittal of Draft ALP Drawing Set to FAA	<b>15 days</b>	<b>Fri 7/14/17</b>	<b>Thu 8/3/17</b>
65	Task 9.2.1 - Preliminary Draft ALP Drawing Set	5 days	Fri 7/14/17	Thu 7/20/17
66	Task 9.2.2 - Draft ALP Drawing Set	5 days	Fri 7/28/17	Thu 8/3/17
67	<b>Task 10.0 - Facilities Implementation Plan</b>	<b>46 days</b>	<b>Wed 5/17/17</b>	<b>Fri 7/21/17</b>
68	Task 10.1 - Project Identification	5 days	Wed 5/17/17	Tue 5/23/17
69	Task 10.2 - Preparation of Final Cost Estimates	10 days	Wed 5/24/17	Wed 6/7/17
70	Task 10.3 - Phasing of Development	15 days	Thu 6/8/17	Wed 6/28/17
71	Task 10.4 - Prepare Working Paper and Conduct Meetings	<b>16 days</b>	<b>Thu 6/29/17</b>	<b>Fri 7/21/17</b>
72	Task 10.4.1 - Prepare Draft Working Paper #4	10 days	Thu 6/29/17	Thu 7/13/17
73	Task 10.4.2 - Attend Coordination/Stakeholders Meeting	1 day	Fri 7/14/17	Fri 7/14/17
74	Task 10.4.3 - Prepare Final Working Paper #4	5 days	Mon 7/17/17	Fri 7/21/17
75	<b>Task 11.0 - Financial Feasibility Analysis</b>	<b>51 days</b>	<b>Fri 7/14/17</b>	<b>Mon 9/25/17</b>
76	Task 11.1 - Prepare Draft Working Paper #5	30 days	Fri 7/14/17	Thu 8/24/17
77	Task 11.2 - Attend Coordination/Stakeholders Meeting	1 day	Fri 9/1/17	Fri 9/1/17
78	Task 11.3 - Prepare Final Working Paper #5	15 days	Tue 9/5/17	Mon 9/25/17
79	<b>Task 12.0 - Prepare Airport Master Plan Update Report and Final ALP</b>	<b>46 days</b>	<b>Tue 9/26/17</b>	<b>Thu 11/30/17</b>
80	Task 12.1 - Preliminary Draft Airport Master Plan Update Report	15 days	Tue 9/26/17	Tue 10/17/17
81	Task 12.2 - Draft Executive Summary	10 days	Wed 10/18/17	Tue 10/31/17
82	Task 12.3 - Final Presentation to Airport Authority	1 day	Wed 11/8/17	Wed 11/8/17
83	Task 12.4 - Draft Airport Master Plan Update Report	10 days	Thu 11/9/17	Wed 11/22/17
84	Task 12.5 - Final Airport Master Plan Update Report and ALP	5 days	Fri 11/24/17	Thu 11/30/17
85	Task 12.6 - Final Executive Summary	<b>4 days</b>	<b>Wed 11/8/17</b>	<b>Mon 11/13/17</b>
86	Task 12.6.1 - List of Deliverables	1 day	Wed 11/8/17	Wed 11/8/17
87	Task 12.6.2 - Summary of Meetings	3 days	Thu 11/9/17	Mon 11/13/17

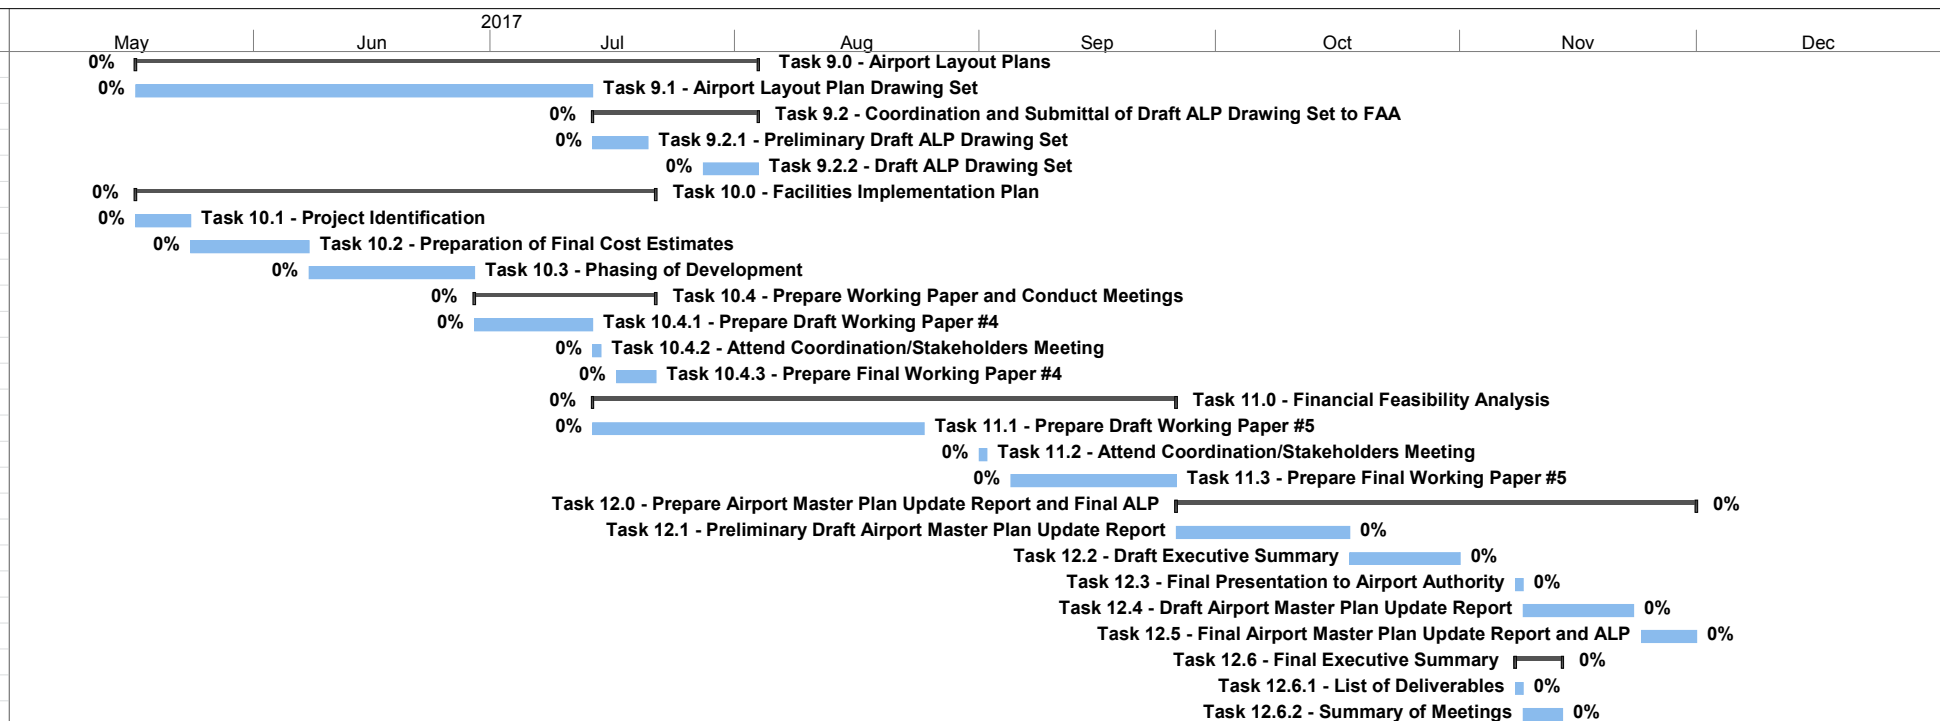


Task		Summary		External Milestone		Inactive Summary		Manual Summary Rollup		Finish-only		Manual Progress	
Split		Project Summary		Inactive Task		Manual Task		Manual Summary		Deadline			
Milestone		External Tasks		Inactive Milestone		Duration-only		Start-only		Progress			

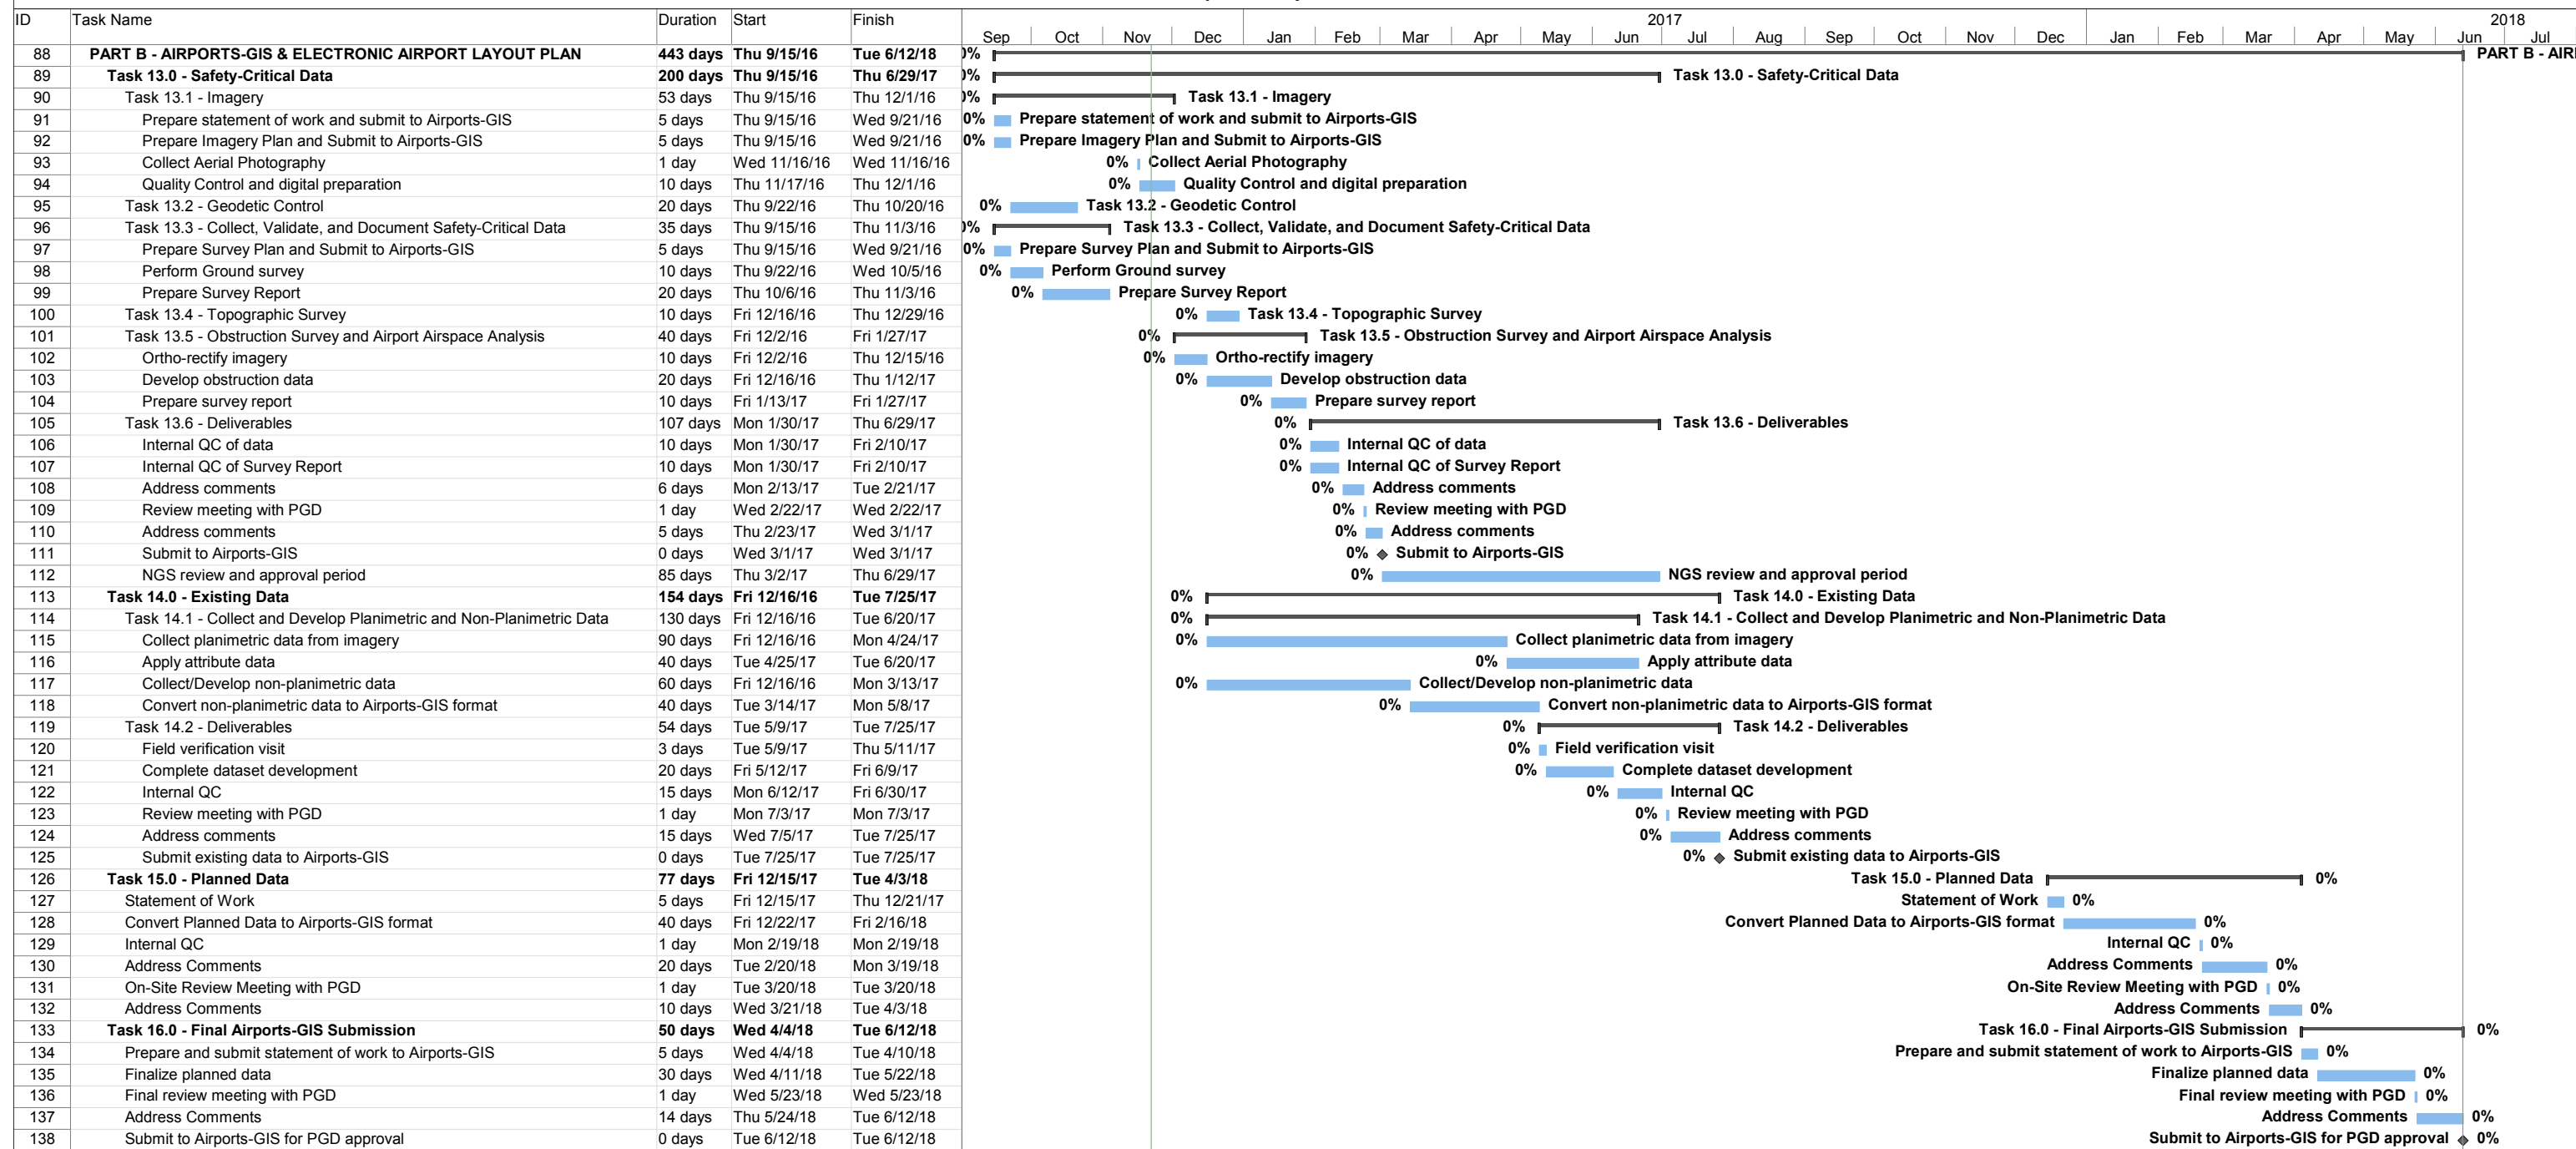

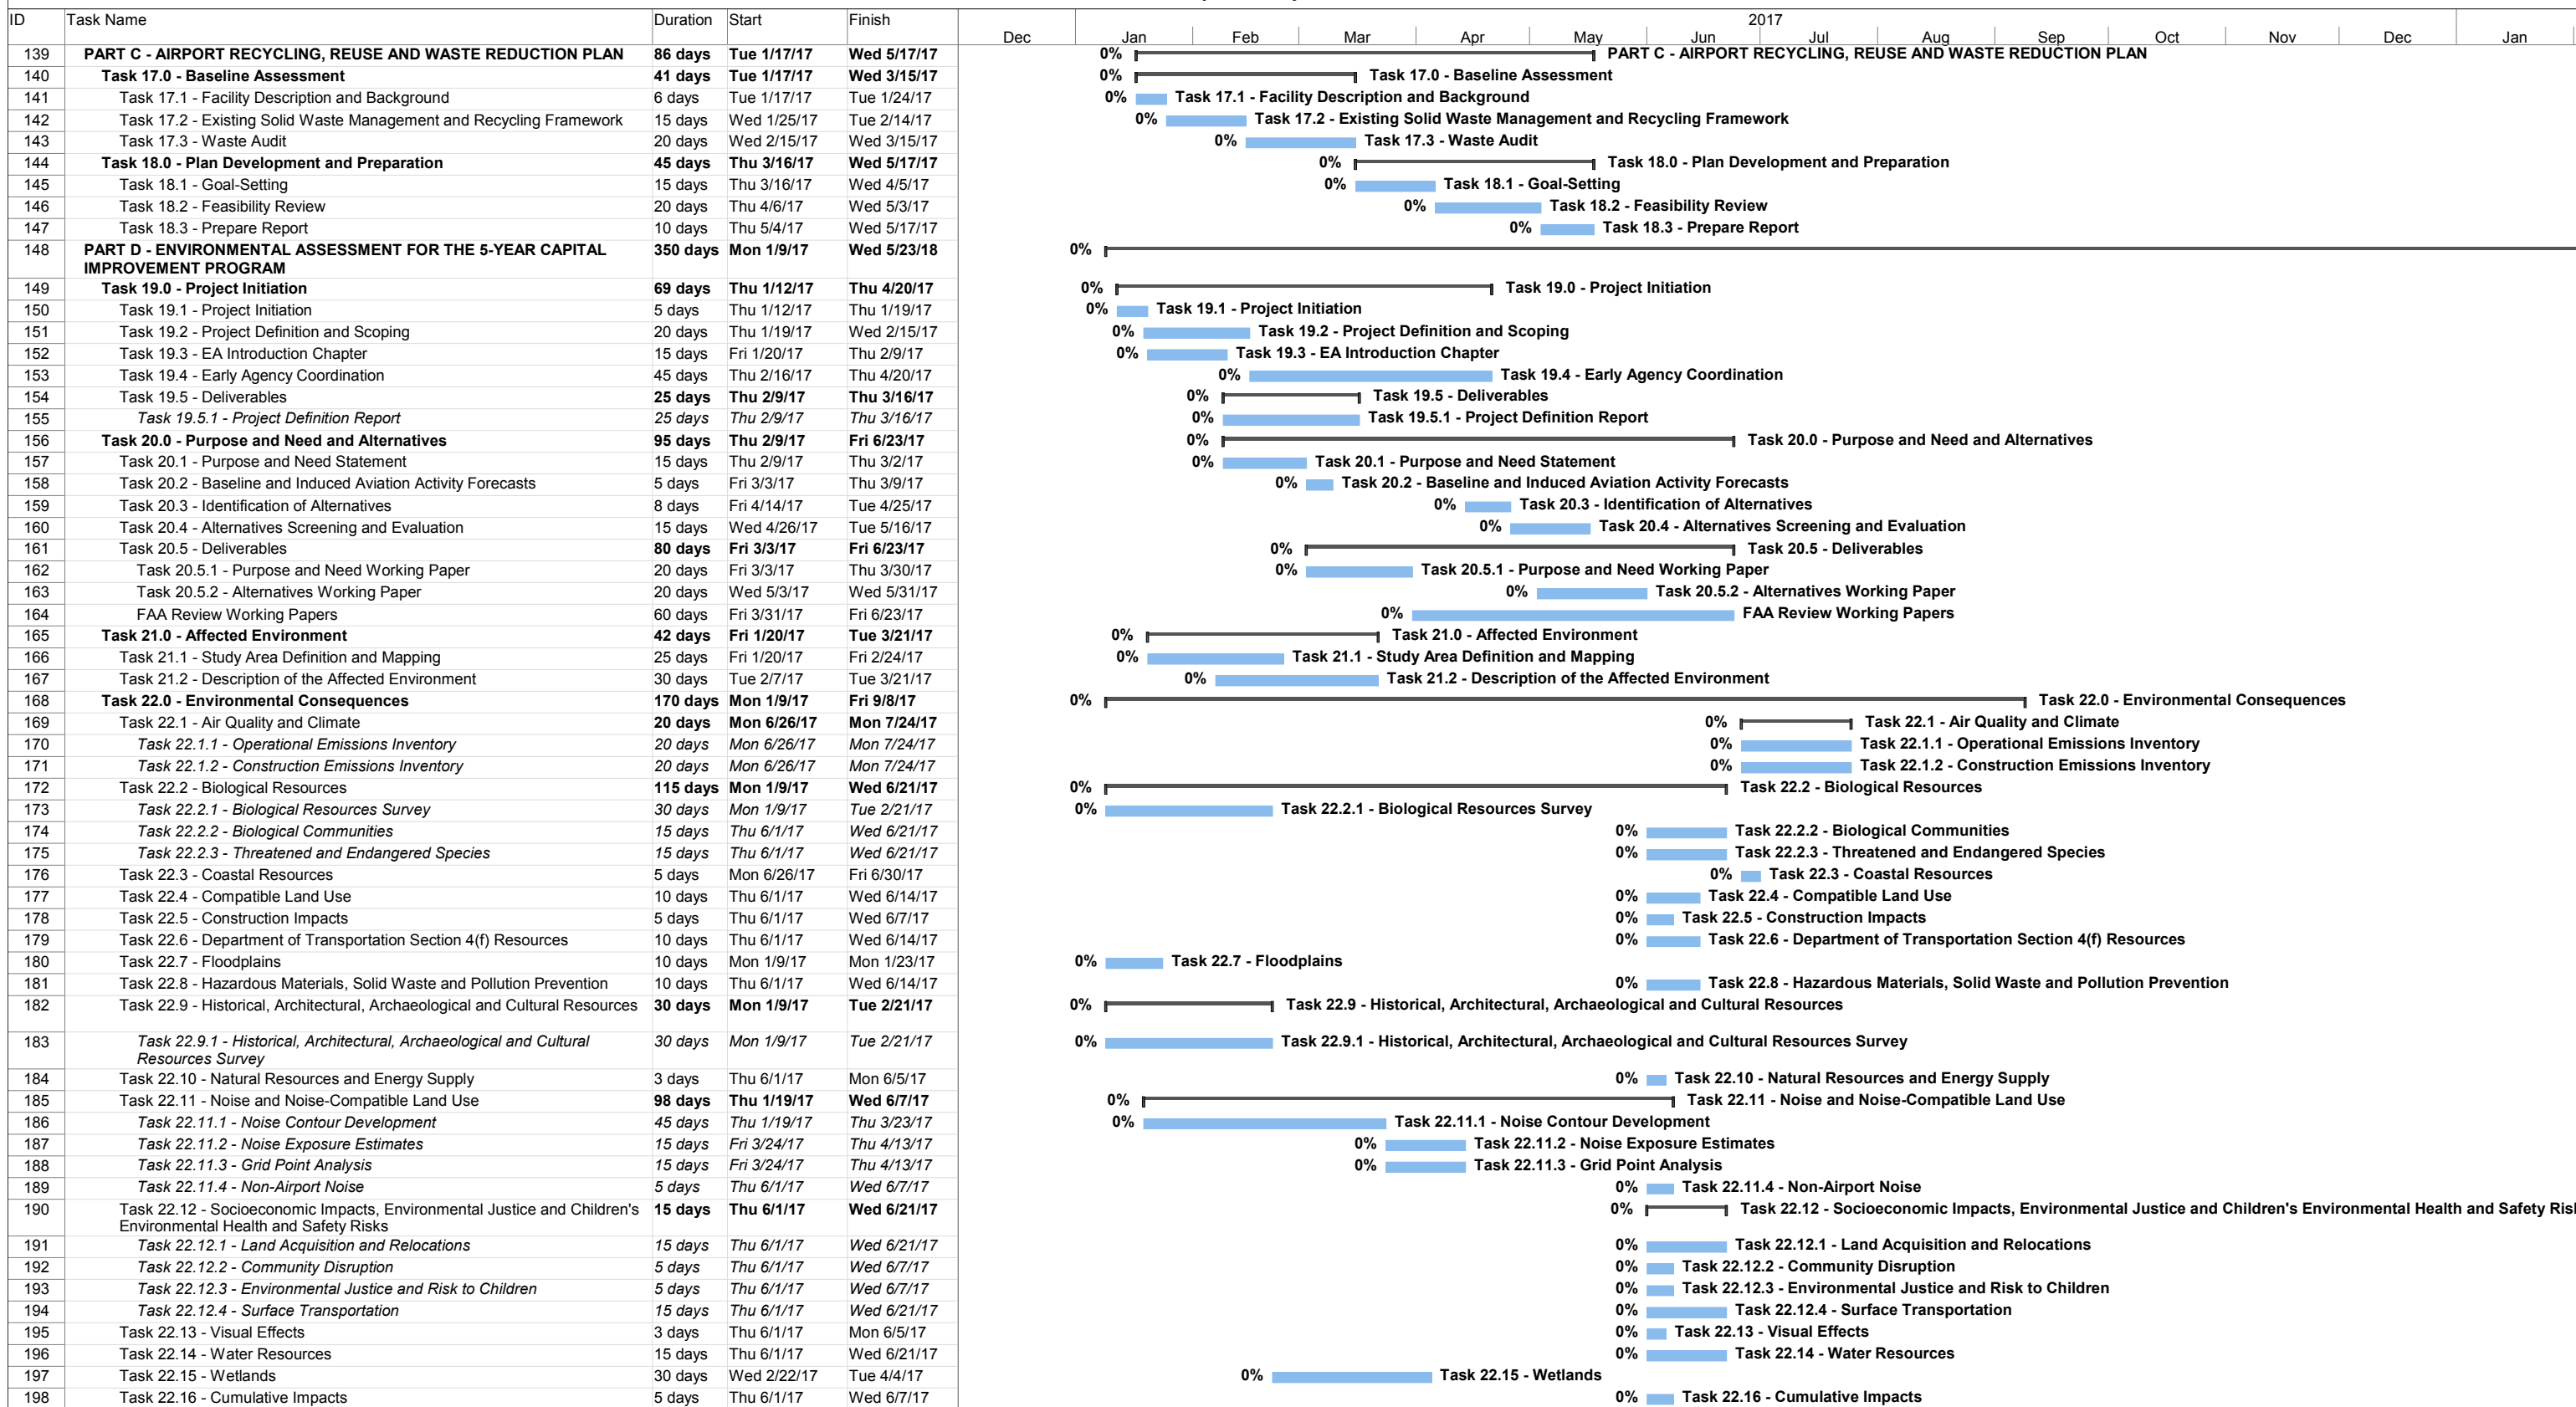

Task		Summary		External Milestone		Inactive Summary		Manual Summary Rollup		Finish-only		Manual Progress	
Split		Project Summary		Inactive Task		Manual Task		Manual Summary		Deadline			
Milestone		External Tasks		Inactive Milestone		Duration-only		Start-only		Progress			

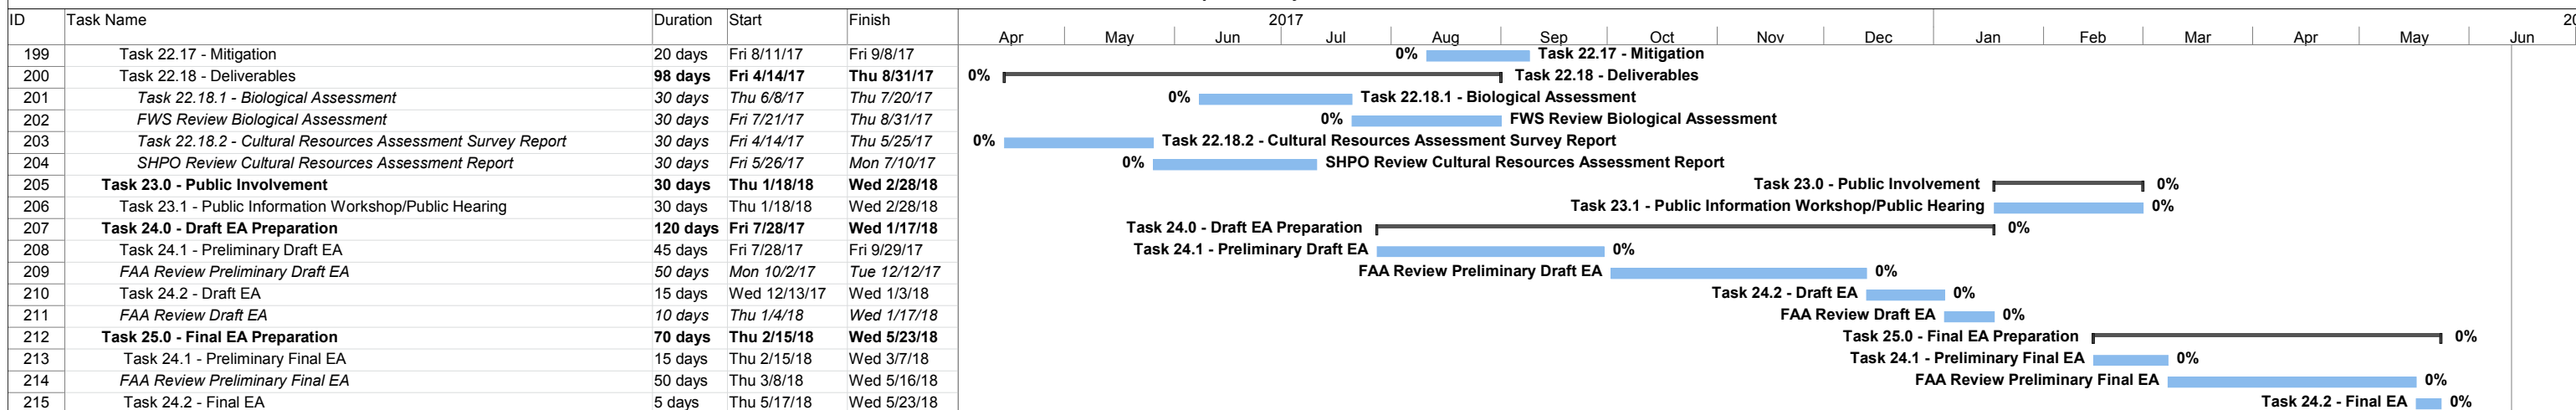

Task		Summary		External Milestone		Inactive Summary		Manual Summary Rollup		Finish-only		Manual Progress	
Split		Project Summary		Inactive Task		Manual Task		Manual Summary		Deadline			
Milestone		External Tasks		Inactive Milestone		Duration-only		Start-only		Progress			
